



The Design Studio, inc.
Architecture + Interior Design

CHANGE ORDER

CO #: 9

Date: 2018.05.10

To: Ray Fertig, Jr.
Recco, Inc DBA Five-R Company
PO Box 20368
Cheyenne, WY 82003

Project Name: Renovation and Expansion of the
Cheyenne Botanic Gardens
OPN: Contract #6219
APN: 13.2.219

You are hereby directed to make the following change(s) in this Contract:

FRIENDS OF THE CHEYENNE BOTANIC GARDENS FOUNDATION FUNDS:

Item #	Description	Reference #	Amount
1	Wood Fence for North Service/Storage yard	COR8	\$11,926.66
2	Floor tile for 3rd floor & VCT for 2nd floor hallway	COR9	\$39,041.00
3	New Aluminum Flagpole	COR10	\$1,815.00
4	Classroom Closet enlargement & Lighting	COR11	\$2,464.00
5	Quartz Countertops (Café, Gift/Info, & Lobby)	COR12	\$20,246.00
6	Gallery Display Rail System (Orangerie & 2nd Floor hall)	COR13	\$4,500.00
7	Additional Hose Bib (Orangerie & Lobby)	COR14	\$983.00
8	Solar Panel system installation assistance	COR15	\$1,000.00
9	Natural Gas line for Patio	PR20	\$4,130.85
10	Additional Countertop & Brackets in Bride's Room	PR38	\$500.00
11	Catering Kitchen: 3 Compartment sink, FRP, & install	PR44	\$5,116.70
TOTAL:			\$91,723.21

Net change by previously authorized Change Orders from The Friends of the Cheyenne Botanic Gardens Foundation Funds:	\$683,870.66
The Friends of the Cheyenne Botanic Gardens Foundation newly generated changes will increase this Change Order in the amount of:	\$91,723.21
The new total Change Order Funding generated by The Friends of the Cheyenne Botanic Gardens Foundation Funds including this Change Order is:	\$775,593.87

The original Contract Guaranteed Maximum Price was:	\$12,300,000.00
Net change by all previously authorized Change Orders:	\$683,870.66
The Contract Guaranteed Maximum Price prior to this Change Order was:	\$12,983,870.66
The Contract Guaranteed Maximum Price will be changed by this Change Order in the amount of:	\$91,723.21
The new Contract Guaranteed Maximum Price including this Change Order:	\$13,075,593.87

The original Date for Substantial Completion was:	2016.11.01
Net change to the Date for Substantial Completion by previously authorized Change Orders:	165 days
The Date of Substantial Completion prior to this Change Order was:	2017.04.15
The Contract Time will be increased by:	108 days
The Date of Substantial Completion as of the date of this Change Order therefore is:	2017.08.01



The Design Studio, inc.
Architecture + Interior Design

CHANGE ORDER

Not valid until signed by the Owner, Architect and Contractor.

ARCHITECT



The Design Studio, inc.
Architecture + Interior Design
1610 Pioneer Avenue
Cheyenne, Wyoming 82001

CONTRACTOR

Recco, Inc DBA Five-R
Company
PO Box 20368

Cheyenne, WY 82003

OWNER

City of Cheyenne Wyoming
Parks and Recreation
2101 O'Neill Avenue, Room 302

Cheyenne, WY 82001

Signed

Randy Byers, AIA, LEED ap

Printed Name

Date

Signed

Ray Fertig, Jr.

Printed Name

Date

Signed

Mayor Marian Orr

Printed Name

Date

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR: Recco, Inc dba Five-R Co.

P.O. Box 20368
Cheyenne, WY 82003

DESCRIPTION OF WORK:	Wood Fence
1. Clearing of site 2. Excavation of foundation 3. Foundation concrete 4. Setting of posts 5. Setting of rails 6. Setting of pickets 7. Finishing of fence	1. Clearing of site 2. Excavation of foundation 3. Foundation concrete 4. Setting of posts 5. Setting of rails 6. Setting of pickets 7. Finishing of fence

PROPOSED CONTRACT PRICE: \$11,926.66

CHANGE ORDER REQUEST NUMBER: 8

WORK LOCATION:
Cheyenne Botanic Gardens Renovation

LINE NO	ITEM	UNIT OF MEASURE	QTY	MATERIAL COST		LABOR COSTS			OTHER DIRECT COSTS	LINE TOTAL
				UNIT	TOTAL	MANHOUR MANDAYS	AVERAGE RATE	TOTAL		
	(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)
1	Cedar privacy fence, double gates:									
2										
3										
4	Cost per Alco Fence proposal attached :									
8	5R Profit/Overhead @ 5%									11,136.00
9	5R Bond/Insurance @ 2%									556.80
10										233.86
11										
12										
13										
14										
15										
TOTALS										\$11,926.66

Exclusions/Clarifications:

ALCO FENCE Co., Inc.

2421 E. 7th Street
Cheyenne, WY 82001

Telephone: (307) 634-2116
Fax: (307) 634-2117

Invoice

Date	Invoice #
8/2/2017	4550

Bill To
Five R Company (Recco, Inc.) Ray Fertig P.O. Box 20368 Cheyenne, WY. 82003

Ship To
Cheyenne Botanic Gardens Conservatory Yard

P.O. Number	Terms	Rep	Ship	Via	F.O.B.	Project
			8/2/2017			Conservatory Yard
Quantity	Item Code	Description			Price Each	Amount
	FENCE 1	171' x 6" cedar privacy fence				10,987.00
	FENCE 1	2- double drive gates				149.00
		Gate frame for roof top shed				0.00
		Sales Tax			5.00%	
RECCO INC DBA FIVE-R CO RECEIVED AUG 7 2017						
JOB # <u>1586</u> PHASE # <u>FENCE RENT</u>						
APPROVED BY <u>[Signature]</u> DATE <u>8/1/17</u>						
PHASE # _____						
Total					\$11,136.00	

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR:	Recco, Inc dba Five-R Co.	ADDRESS:	P.O. Box 20368 Cheyenne, WY 82003
--------------------	---------------------------	-----------------	--------------------------------------

DESCRIPTION OF WORK:	PROPOSED CONTRACT PRICE:
Tile 3rd Floor, 2nd Floor Hall & Prep	\$39,041.00

CHANGE ORDER REQUEST NUMBER: 9	PROJECT NUMBER: PC-428-15-A	WORK LOCATION: Cheyenne Botanic Gardens Renovation
--------------------------------	--------------------------------	---

[illegible]

Exclusions/Clarifications:	
----------------------------	--

42036
8/19/17
\$17,640.36
14657

JOB # 15 BG PHASE # 09300
APPROVED BY [Signature] DATE 8/2/17

RECEIVED
AUG 2 2017

CHEYENNE TILE AND STONE CO., INC.
Tom Evans Tile Contractors Mike Pyle
PHONE : (307) 638-5088 911 East Fox Farm Rd. UNIT # 5 FAX : (307) 638 8432
Cheyenne Wyo. 82007

CERAMIC TILE	MARBLE	GRANITE
--------------	--------	---------

FIVE - R CONSTRUCTION

P.O. BOX 20368

CHEYENNE WY, 82003

DATE	DESCRIPTION	AMOUNT	TOTAL
	ORIGINAL CONTRACT:	\$116,575.00	\$116,575.00
	CHANGE ORDER # 1 (RESTROOM WALL TILE)	\$16,850.00	\$16,850.00 ✓
X	CHANGE ORDER # 2 (STAIR NOSING))	\$12,600.00	\$12,600.00 ✓ 10,000
X	CHANGE ORDER # 3 (VEST. 110 & 123 TILE)	\$1,280.00	\$1,280.00 1280
	CHANGE ORDER # 4 (FLOOR LEVELING)	\$12,344.00	\$12,344.00 ✓ 8571
	CHANGE ORDER # 5 (TILE BENCH)	2,860.00	\$2,860.00
X	CHANGE ORDER # 6 (VCT - 207, 208, & 209)	\$11,230.00	\$11,230.00 11,230
X	CHANGE ORDER # 7 (TILE HALL 301)	\$7,960.00	\$7,960.00 7960
1/19/16	PAYMENT. (BILLING # 1)		-\$33,623.65
3/30/16	PAYMENT. (BILLING # 2)		-\$9,379.83
5/30/17	PAYMENT. (BILLING # 3)		-\$43,089.30
7/26/17	PAYMENT. (BILLING # 4)		-\$61,560.00
	BILLING # 5		
	RE: BOTANIC GARDENS ✓	TOTAL DUE:	\$34,046.22
			- 16,405.86 Ref on hold
			17,640.36

IT'S BEEN A PLEASURE TO WORK WITH YOU!!!

TERMS:
Full payment due within 15 days of billing date.

THANK YOU, CTS.

BILLING DATE : 7/31/17

INVOICE # 5136-E

OK Ref
8.3.17

39,041
33,070
371041

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR: Recco, Inc dba Five-R Co.

ADDRESS:

P.O. Box 20368
Cheyenne, WY 82003

DESCRIPTION OF WORK: New Aluminum Flagpole


PROPOSED CONTRACT PRICE:
\$1,815.00

CHANGE ORDER REQUEST NUMBER: 10

PROJECT NUMBER:
PC-428-15-A

WORK LOCATION:
Cheyenne Botanic Gardens Renovation

[illegible]

**Flagpole Quotation**

Quote Date: September 7, 2017

Quote # 526595

To: Racco Inc. dba Five-R Constuction
Attn: Lisa Barela

Project: Botanic Garden Conservatory (Expansion & Renovation)
CHEYENNE, WY

Quantity	Description	Unit Price	Total Price
1	30' exposed x 33' overall x 7" butt x 0.188" wall Aluminum Cone Tapered Flagpole, Satin Brush Finish, Cam - Internal System, Gold Aluminum Ball, Cam Truck - Revolving, Nylon Halyard, 2-Bronze Chrome-Plated Snaphooks, Internal Cam Cleat, Spun Aluminum Collar, Ground Sleeve Mounting	1,390.00	1,390.00
1	5' x 8' U.S. Nylon Flag	65.00	65.00

NOTE: 1. We Manufacture FLAGPOLES, BANNER POLES, FIRE DEPT SLIDE POLES, ANTENNA POLES AND SPIRES
* Please Fax Specs For All These Products to 631-689-5528 *

Exclusions:

- 1) Licensed Engineering not included outside New York.
2) Quote limited to source listed above.
3) Please notice any notes / options for each product.
4) All permits are by others.

- 5) Does NOT include installation, unless noted above.
6) Freight Charge estimated for single shipment.
7) Orders are subject to 25% cancellation fees.
8) Prices valid for 90 days.

Subtotal: 1,455.00
Freight: 360.00
* Total \$1,815.00

If the above is acceptable, please sign below, and fax back to our office as notice to proceed. Please call if you have any questions. Thank you in advance.

* Tax is not included.
Applied to all orders delivered in NY, NJ and CT only.

Respectfully Submitted,
Carolyn Barbarite

Signed Approval: [Signature]Date: 9-8-17Print Name: Lisa BarelaPO. No. 14CB6Bill To: Five-R CoShip To: CheyenneP.O. Box 20368Cheyenne, WY82003Contact: LisaContact: Randal FertisPhone: 307-638-1966Phone: 307-631-4876

For established accounts in writing, Terms are Net 30. Payment terms for All other orders are Pre-Paid C.O.D.

You may pre-pay by Check or Credit Card. Please be aware that Lead times vary.

* Tax is not included. Applied to all orders delivered in NY, NJ and CT only. Retailers must provide a copy of their release certificates. Certificates must be on file for all tax exempt jobs.

97 Gnarled Hollow Road, East Setauket New York 11733 USA . Web-site: www.poletech.com
Tel: 631.689.5525 . 800.633.6733 . Fax: 631.689.5528 . E-mail: info@poletech.com

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR: Recco, Inc dba Five-R Co.

P.O. Box 20368

Cheyenne, WY 82003

DESCRIPTION OF WORK:	Classroom Closet Enlargement & Lighting
1. Remove existing closet doors and hardware. 2. Enlarge closet opening by 4 feet. 3. Install new closet doors and hardware. 4. Install new lighting fixture. 5. Paint closet interior and exterior.	

PROPOSED CONTRACT PRICE:

\$2,464.00

CHANGE ORDER REQUEST NUMBER: 11

PROJECT NUMBER:

PC-428-15-A


Chevenne Botanic

BOR COSTS	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	
44	
45	
46	
47	
48	
49	
50	
51	
52	
53	
54	
55	
56	
57	
58	
59	
60	
61	
62	
63	
64	
65	
66	
67	
68	
69	
70	
71	
72	
73	
74	
75	
76	
77	
78	
79	
80	
81	
82	
83	
84	
85	
86	
87	
88	
89	
90	
91	
92	
93	
94	
95	
96	
97	
98	
99	
100	

[illegible]

Exclusions/Clarifications:

CONSTRUCTION COST ESTIMATE BREAKDOWN										May 9, 2018	
CONTRACTOR:		Recco, Inc dba Five-R Co.		ADDRESS:		P.O. Box 20368 Cheyenne, WY 82003					
DESCRIPTION OF WORK:		Quartz Countertop		PROJECT NUMBER:		PC-428-15-A					
CHANGE ORDER REQUEST NUMBER:		12		WORK LOCATION:		Cheyenne Botanic Gardens Renovation					
				MATERIAL COST		LABOR COSTS		OTHER DIRECT COSTS		LINE TOTAL	
LINE NO	ITEM (1)	UNIT OF MEASURE (2)	QTY (3)	UNIT (4)	TOTAL (5)	MANHOUR MANDAYS (6)	AVERAGE RATE (7)	TOTAL (8)	(9)	(10)	
1	Quartz countertops (café, gift/info & lobby):										
2											
3											
4	Cost per Eggli Bros. proposal attached :									20,246.00	
8	5R Profit/Overhead @ 5%									0.00	
9	5R Bond/Insurance @ 2%									0.00	
10											
11											
12											
13											
14											
15											
TOTALS										\$20,246.00	
Exclusions/Clarifications:											



Egli Bros. Millwork, Inc.

120 Daffodil St.
Lander, WY 82520
Phone (307) 332-3000 Fax (307) 332-9270

March 13, 2017

Five R Co.

Re: Cheyenne Botanical Gardens
Change Order #Quartz

Gentlemen

We are pleased to provide a quote for the following item(s);

- Change top in gift area from solid surface to quartz (Cambria cardiff cream)
- Change tops in Lobby Desk 111 from solid surface to quartz (Cambria Cardiff cream)
- Add quartz tops to Café 113 (Cambria Cardiff cream)
- Lead time TBD, approximately 8 weeks after receipt of confirmed change order and color selection

OK
3.14.17

This Change Order ADD: \$20,246.00 (sales tax included)

Terms and conditions per original quote

Terms and conditions of this quote;
Same As Original Quote
Quote Good For 10 Days

Please sign and return one copy of this change order as soon as possible. We are unable to proceed with the above changes without this authorization.

The above changes are approved at the price quoted;

Sincerely,

Al Egli

Al Egli
President

Signed _____

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR: Recco, Inc dba Five-R Co.

ADDRESS: P.O. Box 20368
Cheyenne, WY 82003

DESCRIPTION OF WORK:	Gallery Display Rail System
-----------------------------	-----------------------------

PROPOSED CONTRACT PRICE:
\$4,500.00

CHANGE ORDER REQUEST NUMBER:	13	PROJECT NUMBER:	PC-428-15-A
------------------------------	----	-----------------	-------------

Cheyenne Botanic Gardens Renovation

[illegible]

Exclusions/Clarifications:

Gallery System Art Displays, Inc.

Tel: 781 237 8856 Fax: 781 237 8859

345 Linden Street

Wellesley, MA 02481

Invoice

DATE	UC Order No.	INVOICE #
7/14/2017		33002

BILL TO
Recco, Inc. Construction Company P. O. Box 20368 Cheyenne, WY 82003 Att: Lisa Barela

PAID
07/14/2017

SHIP TO
Cheyenne Botanic Gardens 710 South Lions Park Drive Cheyenne, WY 82001

P.O. NUMBER	TERMS	REP	SHIP	VIA	AM Order No.
Phone	Pd Credit Card	RLZ	7/14/2017	Ground	

QUANTITY	ITEM CODE	DESCRIPTION	PRICE EACH	AMOUNT
24	TR2	Anodized Track - 2 meter length (6.5ft)	24.50	588.00
12	EndcapA	End Caps for anodized track	0.90	10.80
5	HAsc2	Hangers, stainless steel cable (2 meter) - pack of 10	68.50	342.50
5	HOsg	Hooks - self-gripping, for stainless steel cable only - ten pack	77.00	385.00
	Shipping	Packing and shipping	71.68	71.68
	Payment Received	Visa Card Ending 8126 Thank you		

Please remit all payments to: Gallery System Art Displays, 1150
N. Gale Mountain Road, Pocatello, ID 83204

Total \$1,397.98

Gallery System Art Displays, Inc.

345 Linden Street

Wellesley, MA 02481

Tel: 781 237 8856 Fax: 781 237 8859

Invoice

DATE	UC Order No.	INVOICE #
10/10/2017		33688

BILL TO
Recco, Inc. Construction Company P. O. Box 20368 Cheyenne, WY 82003 Att: Lisa Barela

PAID
10/10/2017

SHIP TO
Cheyenne Botanic Gardens 710 South Lions Park Drive Cheyenne, WY 82001

P.O. NUMBER	TERMS	REP	SHIP	VIA
Phone	Pd Credit Card	AS	10/10/2017	Ground

AM Order No.

QUANTITY	ITEM CODE	DESCRIPTION	PRICE EACH	AMOUNT
24	TR2	Anodized Track - 2 meter length (6.5ft)	24.50	588.00
5	HAsc2	Hangers, stainless steel cable (2 meter) - pack of 10	68.50	342.50
5	HOsg	Hooks - self-gripping, for stainless steel cable only - ten pack	77.00	385.00
25	EndcapA	End Caps for anodized track	0.90	22.50
	Shipping	Packing and shipping	71.68	71.68
	Payment Received	VISA Card Ending8126. Thank you		

Please remit all payments to: Gallery System Art Displays, 1150
N. Gale Mountain Road, Pocatello, ID 83204

Total \$1,409.68

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

CONTRACTOR: Recco, Inc dba Five-R Co.

P.O. Box 20368
Cheyenne, WY 82003

DESCRIPTION OF WORK:	Additional Hose Bib (Orangerie & 2nd Floor Hall

PROPOSED CONTRACT PRICE:
\$983.00

CHANGE ORDER REQUEST NUMBER: 14

PROJECT NUMBER:
PC-428-15

WORK LOCATION:
Cheyenne Botanic Gardens Renovation

[illegible]

Exclusions/Clarifications:

TOWN & COUNTRY PLUMBING, INC.

145 S. MAIN
P.O. BOX 340
BURNS, WY 82053

Invoice**Invoice #:** 3849**Invoice Date:** 5/10/2017**Due Date:** 6/9/2017**Project:****P.O. Number:****Bill To:**

Recco, Inc. dba 5-R Co.
P.O. Box 20368
Cheyenne, WY 82003

Description	Hours/Qty	Rate	Amount
Botanic Gardens - extra for Recco, Inc. - install wall boxes in the Orangerie			
Material		526.00	526.00
Labor		350.00	350.00
All work is complete!			
Total			\$876.00
Payments/Credits			\$0.00
Balance Due			\$876.00

CONSTRUCTION COST ESTIMATE BREAKDOWN

May 9, 2018

Recco, Inc dba Five-R Co.

ADDRESS:

P.O. Box 20368

Cheyenne, WY 82003

WORK: Solar Panel System

PROPOSED CONTRACT PRICE:

QUEST NUMBER: 15

PROJECT NUMBER:

PC-428-15-A

WORK LOCATION:

Cheyenne Botanic Gardens Renovation

LINE NO	ITEM	UNIT OF MEASURE	QTY	MATERIAL COST		LABOR COSTS			OTHER DIRECT COSTS	LINE TOTAL
				UNIT	TOTAL	MANHOUR MANDAYS	AVERAGE RATE	TOTAL		
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	
1	Solar panel system installation assistance:									
2										
3										
4	5R Equipment								388.00	
5	5R Labor:								612.00	
6	5R Profit/Overhead @ 5%								0.00	
7	5R Bond/Insurance @ 2%								0.00	
8										
9										
10										
11										
09k										
98 im										
TOTALS									\$1,000.00	

Exclusions/Clarifications:

CONSTRUCTION COST ESTIMATE BREAKDOWN											DATE: September 15, 2016
CONTRACTOR: Recco, Inc dba Five-R Co.		ADDRESS:		P.O. Box 20368 Cheyenne, WY 82003							
DESCRIPTION OF WORK: Natural Gas Line to Patio				PROPOSED CONTRACT PRICE: 4,130.85							
PROPOSAL REQUEST NUMBER: 20		PROJECT NUMBER: Contract #6219		WORK LOCATION: Cheyenne Botanic Gardens Conservatory							
LINE NO	ITEM (1)	UNIT OF MEASURE (2)	QTY (3)	UNIT (4)	TOTAL MATERIAL COST (5)	MANHOUR MANDAYS (6)	AVERAGE RATE (7)	TOTAL (8)	OTHER DIRECT COSTS (9)	LINE TOTAL (10)	
	Reference attached PDF with proposed routing from Children's Village natural gas meter located on the north side of the building. Final termination location will be field coordinated from owner/architect.										
	John Parks; MKK Engineers: "Connect the new 1" gas pipe to the existing gas header at the existing meter located at the N.E. corner of the Children's Village. Install 1" gas cock and drop a 1" cathodic protected steel gas pipe to 30" (minimum) depth. Provide Polyethylene PE pipe, ASTM D-2513, connected to seal pipe and run to the new Plaza as shown on Drawing A-113. Coordinate final routing with existing utilities and the Architect. Bed and cover new PE pipe in the sand and provide a locator tape with copper tracer wire. At location determined by the Architect, connect to 1" cathodic protected steel pipe riser to above concrete slab with gas cock and cap."										
1											
2											
3											
4											
5											
6											
7	Costs per Town & Country Plumbing proposal attached:										
8	5R Profit/Overhead @ 5%									3,857.00	
9	5R Bond/Insurance @ 2%									192.85	
10										81.00	
11											
12											
13											
14											
15											
TOTALS										4,130.85	
Exclusions/Clarifications:											

Proposal

TOWN & COUNTRY PLUMBING, INC.
145 S. Main
Burns, WY 82053
(307) 547-3579 Fax (307) 547-9246

Page No. 1 of 1 page(s)

PROPOSAL SUBMITTED TO: Recco Inc. dba SR	PHONE:	Date: August 26, 2016
STREET:	JOB NAME: Cheyenne Botanic Gardens Conservatory Re-bld	
CITY, STATE AND ZIP CODE:	JOB LOCATION: Cheyenne, WY	
ARCHITECT: TDSI	DATE OF PLANS: 2/06/15	JOB PHONE:

We hereby submit estimates for: PR #0020 add gas line to patio

WE PROPOSE hereby to furnish material and labor-complete in accordance with plans, specifications and the above scope, for the sum of:

Three Thousand Eight Hundred Fifty-Seven and 00/100-----\$3,857.00

Payment to be made as follows: 100% of approved monthly estimates.

This proposal must be included in any contract between the contractor and Town & Country Plumbing, Inc.

All material is guaranteed to be as specified. All work to be completed in a workmanlike manner according to standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workman's Compensation Insurance.

Authorized
Signature

Justin Smith

Note: This proposal may be withdrawn by Town & Country Plumbing Inc. if not notified of acceptance within 10 days from the date of this proposal.

Acceptance of Proposal – The above prices, specifications
And conditions are satisfactory and are hereby accepted.
You are authorized to do the work as specified.

Signature_____

Date of Acceptance: _____

Signature_____

CONSTRUCTION COST ESTIMATE BREAKDOWN										DATE:	May 10, 2018							
CONTRACTOR:		Recco, Inc dba Five-R Co.		ADDRESS:		P.O. Box 20368 Cheyenne, WY 82003		PROPOSED CONTRACT PRICE:			500.00							
DESCRIPTION OF WORK:		Brides Room 224: Additional Counter Top & Brackets		PROJECT NUMBER:		Contract #6219		WORK LOCATION:			Cheyenne Botanic Gardens Conservatory							
PROPOSAL REQUEST NUMBER:		38		UNIT OF MEASURE		QTY		MATERIAL COST		LABOR COSTS								
LINE NO	ITEM	UNIT OF MEASURE	(2)	(3)	UNIT	(4)	TOTAL	(5)	MANHOUR MANDAYS	(6)	AVERAGE RATE	(7)	TOTAL	(8)	OTHER DIRECT COSTS	(9)	LINE TOTAL	(10)
	Provide cost to furnish and install additional counter top on South wall of Brides room 224, West of existing sink & base cabinet. Additional counter top dimensions: 96" long, 1.56" thick, match depth of existing base cabinet. Color: Kensington Maple 1077660.																	
1	Provide additional brackets to support counter top to wall:																	
2																		
3																		
4																		
6	Costs per Eggli Bros. Millwork proposal attached:																	
7	5R Bond/Insurance @ 2%																	500.00
8	5R Profit @ 5%																	0.00
9	5R Overhead @ 5%																	0.00
10																		
11																		
12																		
13																		
TOTALS																		500.00
Exclusions/Clarifications:																		

Lisa Barela

From: Al Eggli <al@egglibros.com>
Sent: Tuesday, July 25, 2017 9:30 AM
To: recco@fivercompany.com
Subject: RE: Botanic Gardens

Lisa,

I am not certain if I ever gave you pricing on the items that you had sent to me.

Here are the prices.

Keep in mind that these are FOB our shop. Not sure of the best way to get them to you. Freight or delivery would be extra or you could pick them up.

Sales Tax included.

- 1) New 96" top at room 224: \$315.00
- 2) New 101" long backsplash for room 225: N/C
- 3) New Aluminum channel for reception desk: N/C
- 4) New 7'-7½" coat rack: \$252.00

315 TOP
85 BRACKET
100 SHIPPING

Let me know. I will have to order material.

Thanks,

Al Eggli

President
Eggli Bros. Millwork, Inc.
120 Daffodil St
Lander, WY. 82520
Ph. 307-332-3000

From: Lisa Barela [<mailto:recco@fivercompany.com>]
Sent: Monday, July 24, 2017 3:00 PM
To: al@egglibros.com; 'Jessica Wooten' <jessica@egglibros.com>
Subject: Botanic Gardens

Please find attached Change Order No. 3. Please review, fill out, sign, and email back. Call if any questions. Have a great day.

Thank you.

Lisa Barela
Recco, Inc. dba Five-R Co.
P.O. Box 20368
Cheyenne, WY 82003
307-638-7566 voice
307-632-1960 fax
recco@fivercompany.com

CONSTRUCTION COST ESTIMATE BREAKDOWN

DATE: **March 30, 2018**

CONTRACTOR: Recco, Inc dba Five-R Co.

ADDRESS:

P.O. Box 20368

Cheyenne, WY 82003

DESCRIPTION OF WORK:	Catering Kitchen
-----------------------------	-------------------------

PROPOSED CONTRACT PRICE:**PROPOSAL REQUEST NUMBER: 44**

PROJECT NUMBER:

T NUMBER:

WORK LOCATION:

Cheyenne Botanic Gardens Conservatory

LINE NO	ITEM	UNIT OF MEASURE	QTY	MATERIAL COST		LABOR COSTS			OTHER DIRECT COSTS	LINE TOTAL
				UNIT	TOTAL	MANHOUR MANDAYS	AVERAGE RATE	TOTAL		
1	Catering kitchen: 3 compartment sink, FRP, and install									
2										
3										
4										
5	Costs per Town & Country Plumbing proposal attached									
6	5R Materials / Labor:					500.00	35	36.00	1,260.00	2,790.00
7	5R Bond/Insurance @ 2%									91.00
8	5R Profit @ 5%									232.05
9	5R Overhead @ 5%									243.65
10										
11										
12										
	TOTALS									5,116.70
Exclusions/Clarifications:										

Proposal

TOWN & COUNTRY PLUMBING, INC.
145 S. Main
Burns, WY 82053
(307) 547-3579 Fax (307) 547-9246

Page No. 1 of 4 page(s)

PROPOSAL SUBMITTED TO: Recco Inc. dba SR	PHONE:	Date: April 6, 2018
STREET:	JOB NAME: Cheyenne Botanic Gardens Conservatory Re-bid	
CITY, STATE AND ZIP CODE:	JOB LOCATION: Cheyenne, WY	
ARCHITECT: TDSI	DATE OF PLANS: 2/06/15	JOB PHONE:

We hereby submit estimates for:

Supply Elkay 14-3C16X20-L-18X three compartment sink with one T&S brass B-0133-ADF12-B pre-rinse faucet.

Note: Please specify right or left drain board.

Attachment: specification sheets.

WE PROPOSE hereby to furnish material and labor-complete in accordance with plans, specifications and the above scope, for the sum of:

Two Thousand Seven Hundred Ninety and 00/100-----\$2,790.00

Payment to be made as follows: 100% of approved monthly estimates.

This proposal must be included in any contract between the contractor and Town & Country Plumbing, Inc.

All material is guaranteed to be as specified. All work to be completed in a workmanlike manner according to standard practices. Any alteration or deviation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workman's Compensation Insurance.

Authorized
Signature

Note: This proposal may be withdrawn by
Town & Country Plumbing Inc. if not
notified of acceptance within 10 days
from the date of this proposal.

Acceptance of Proposal - The above prices, specifications
And conditions are satisfactory and are hereby accepted.
You are authorized to do the work as specified.

Signature _____

Date of Acceptance: _____

Signature _____




S-1

SPECIFICATION SHEET

Item No.: _____ Qty. _____

Model No.: _____

Project No.: _____

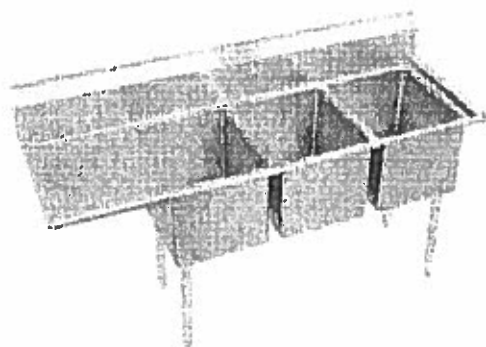

Specifications

14" Standard Series Sink, with three compartments, left drainboard, 9" backsplash, 16 gauge, 300 series stainless steel top and bowl, galvanized legs & adjustable feet, raised 1-1/2" rolled edge, includes 3-1/2" basket strainer, NSF approved

Features

- 16 Ga. stainless steel
- Welded construction for consistent metal gauge thickness throughout
- 14" (355.6 mm) deep tub with 3/4" (19.1 mm) covered radius tub corners
- Drainboard is die stamped for positive drainage
- 9" (228.6 mm) backsplash with tile ledge for easy installation
- Raised 1-1/2" (38.1 mm) rolled edge
- 3-1/2" (88.9 mm) drain with basket strainers included
- 1-5/8" (41.3 mm) galvanized legs with 1" (25.4 mm) adjustable plastic feet
- 2" (50.8 mm) divider between each tub

Flyer Product

In keeping with our policy of continuing product improvement, Elkay SSP reserves the right to change product specifications without notice.

Elkay SSP
421 N. Freya St.
Spokane, WA 99205
Phone: 800-726-0553 Fax: 509-535-1493

SNK-143CLX13MAY2011

14" Standard Series Sinks

14" Deep Standard Series Three Compartment Stainless Steel Sinks

- ☒ 14-3C16X20-L-18X
- ☐ 14-3C18X24-L-18X
- ☐ 14-3C18X24-L-24X
- ☐ 14-3C24X24-L-24X

Options

- ☐ Faucets
- ☐ Tub Accessories
- ☐ Undershelves
- ☐ Rotary Drain Options
- ☐ H-Frame Stainless Steel Legs
- ☐ Stainless Steel Feet Options (bullet & flange styles)

Materials

- Sink & Bowl: 16 Ga. 300 series stainless steel
- Top: Drainboard and backsplash are 16 gauge 300 series stainless steel.
- Legs: All sinks furnished with 1-5/8" (41.3 mm) diameter heavy gauge galvanized tubing with plated galvanized leg gussets and high impact corrosion resistant fully adjustable 1" (25.4 mm) feet.

Mechanical

- 1-1/8" (38mm) faucet holes on 8" (203mm) centers
- 3-1/2" (89mm) waste drain opening



AUTOQUOTES



This specification describes an Elkay SSP product with design, quality and functional benefits to the user. When making a comparison of other producers' offerings, be certain these features are not overlooked.

Website: www.sspinc.net
Email: sspsales@elkay.com
©2011 SSP INC.

Page 1 of 2

Elkay SSP - Sinks - 14" Standard Series Sinks - 3 Compartment - Left Drainboard

A.I.A. File No. 35-C-13





S-1


Item No.: _____ Qty. _____
 Model No.: _____
 Project No.: _____

14" Standard Series Sinks

14" Deep Standard Series Three Compartment Stainless Steel Sinks

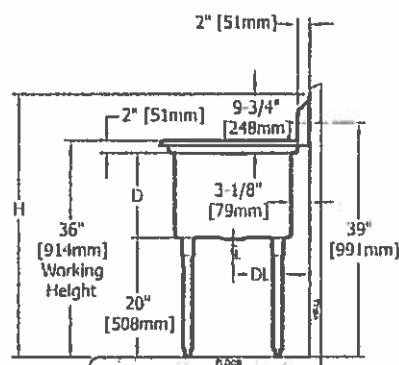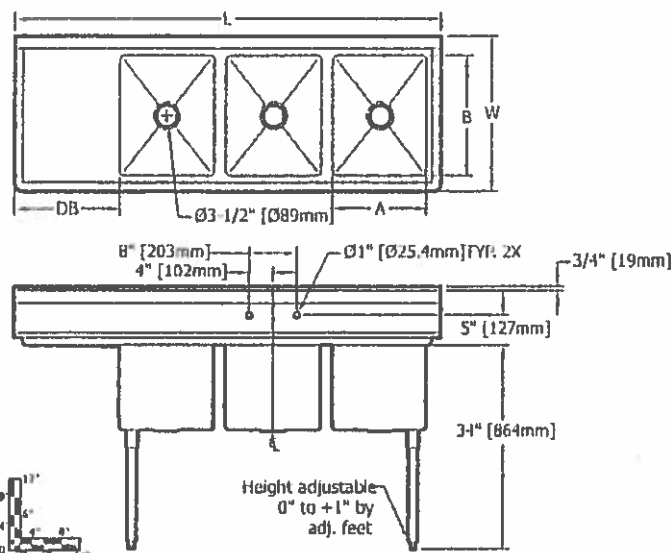

14" Standard Series Sinks																			
Model Number	Bowl Dimensions						Overall Size				Drainboard		Drain	Weight					
	Width		Front-to-Back		Depth		Length		Width		Height		Location	Size	Location				
	in.	mm	in.	mm	in.	mm	in.	mm	in.	mm	in.	mm		in.	mm	lbs.	kg		
14 3C 16 X 20 L 18 X	16	406	20	508	14	356	72.5	1842	25.8	656	43.8	1111	Left	18	457	13	330	284	129
14 3C 18 X 24 L 18 X	18	457	24	610	14	356	78.5	1994	29.8	757	43.8	1111	Left	18	457	15	381	326	148
14 3C 18 X 24 L 24 X	18	457	24	610	14	356	84.5	2146	29.8	757	43.8	1111	Left	24	610	15	381	334	151
14 3C 24 X 24 L 24 X	24	610	24	610	14	356	102.5	2604	29.8	757	43.8	1111	Left	24	610	15	381	403	183



Elkay SSP
 421 N. Freya St.
 Spokane, WA 99205
 Phone: 800-726-0553 Fax: 509-535-1493

SNK-143CLX13MAY2011

Website: www.sspinc.net
 Email: sspsales@elkay.com
 ©2011 SSP INC.



Pre-Rinse Units

B-0133-ADF12-B


TAG: S-1

EasyInstall Pre-Rinse Unit

Architect/Engineering Specifications:

8" wall mount mixing faucet with polished chrome plated brass body, add-on faucet with compression cartridge and lever handle, 12" swing nozzle with stream regulator outlet, 18" riser, 44" flexible stainless steel hose with heat resistant handle, 1.42 GPM spray valve, compression cartridges with spring checks, lever handles, 1/2" NPT female inlets, 6" adjustable wall bracket, spray valve holder and overhead spring. Certified to ASME A112.18.1/CSA B125.1, NSF 61-Section 9 & NSF 372. EPA Act 2005 compliant.

Job Name _____
Model Specified _____ Quantity _____
Variations Specified _____
Date _____

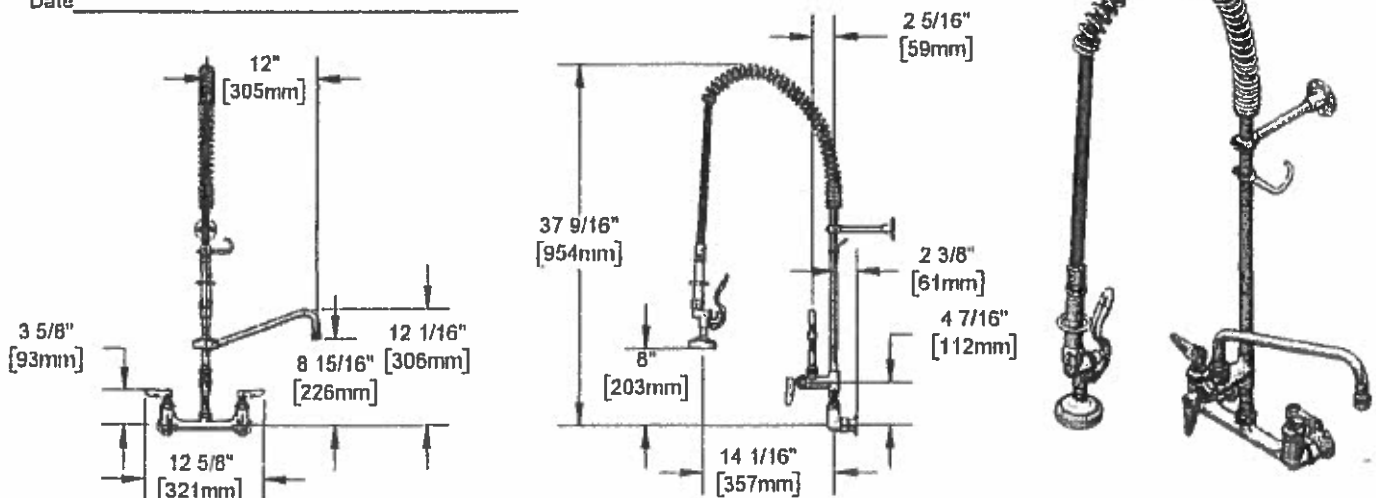

Features & Benefits:

- 8" wall mount mixing faucet w/ polished chrome plated brass body
- EasyInstall add-on faucet w/ polished chrome plated brass body
- 12" swing nozzle w/ stream regulator outlet, Series 1
- 18" rigid riser
- 44" flexible stainless steel hose with heat resistant gray handle and hold down ring
- 1.42 GPM spray valve
- Quarter-turn Eterna compression cartridges with spring checks to prevent cross flow of water
- Lever handles w/ color coded indexes
- 1/2" NPT female eccentric inlets with Ø 2" flanges
- Adjustable centers from 7 3/4" to 8 1/4"
- 6" adjustable wall bracket
- Material: Polished chrome plated brass body, tubular nozzle, add-on faucet body, riser & spray valve body, stainless steel hose and chrome plated metal handles

Product Compliance:

- ASME A112.18.1 / CSA B125.1
- NSF 61 - Section 9
- NSF 372 (Low Lead Content)
- EPA Act 2005 (PRSV)



Warranty: Three Year (Limited)

Performance Data:

- Pressure: 20 - 125 psi
- Temperature: 40°F - 140°F
- Flow Rate:
 - Spray Valve: 1.42 GPM @ 60 psi
 - Add-On Faucet: 9.73 GPM @ 60 psi

Optional Add-On Faucet Outlets (Series 1 / VR Series 6)

GPM	Aerated	VR Aerated (VR Laminar)
1.0	☐ B-0199-01-F10	☐ B-0199-06-F10
1.5	☐ B-0199-01-WS	☐ B-0199-06-WS
2.2	☐ B-0199-01	☐ B-0199-06

Optional Cartridges With Checks

- ☐ Quarter-Turn Cerama w/ Check Valve
- ☐ Quarter-Turn Eterna w/ Spring Check (Standard)

Optional Pre-Rinse Spray Valves

- ☐ B-0107 (1.42 GPM)(Standard)
- ☐ B-0107-C (0.65 GPM)
- ☐ B-0107-J (1.07 GPM)
- ☐ B-0108 (1.07 GPM)
- ☐ B-0108-C (0.65 GPM)

Optional Handles

- ☐ 4" Wrist Action
- ☐ Lever (Standard)
- ☐ 4-Arm



T&S BRASS AND BRONZE WORKS, INC.



• 2 Saddleback Cove • Travelers Rest, SC 29690
Ph 800-476-4103 • Fax 864-834-3518
• Simi Valley, CA • Ph 800-423-0150 • www.tsbrass.com

Date: 02/28/18
